B944 grantt944bwy2008

44.3897 -110.5438 2364.6 m

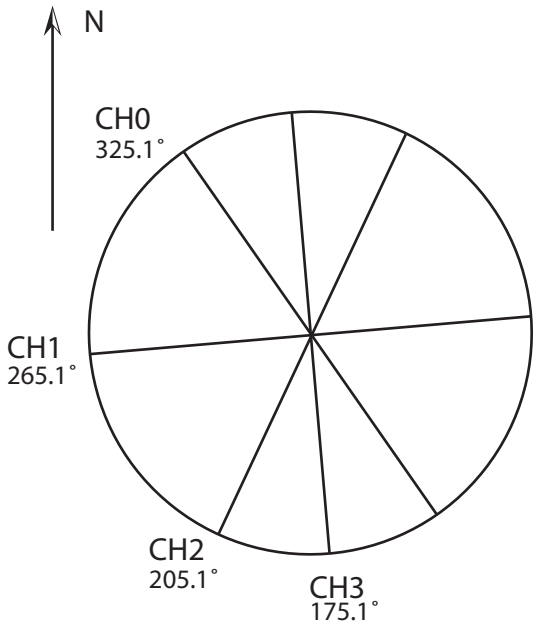

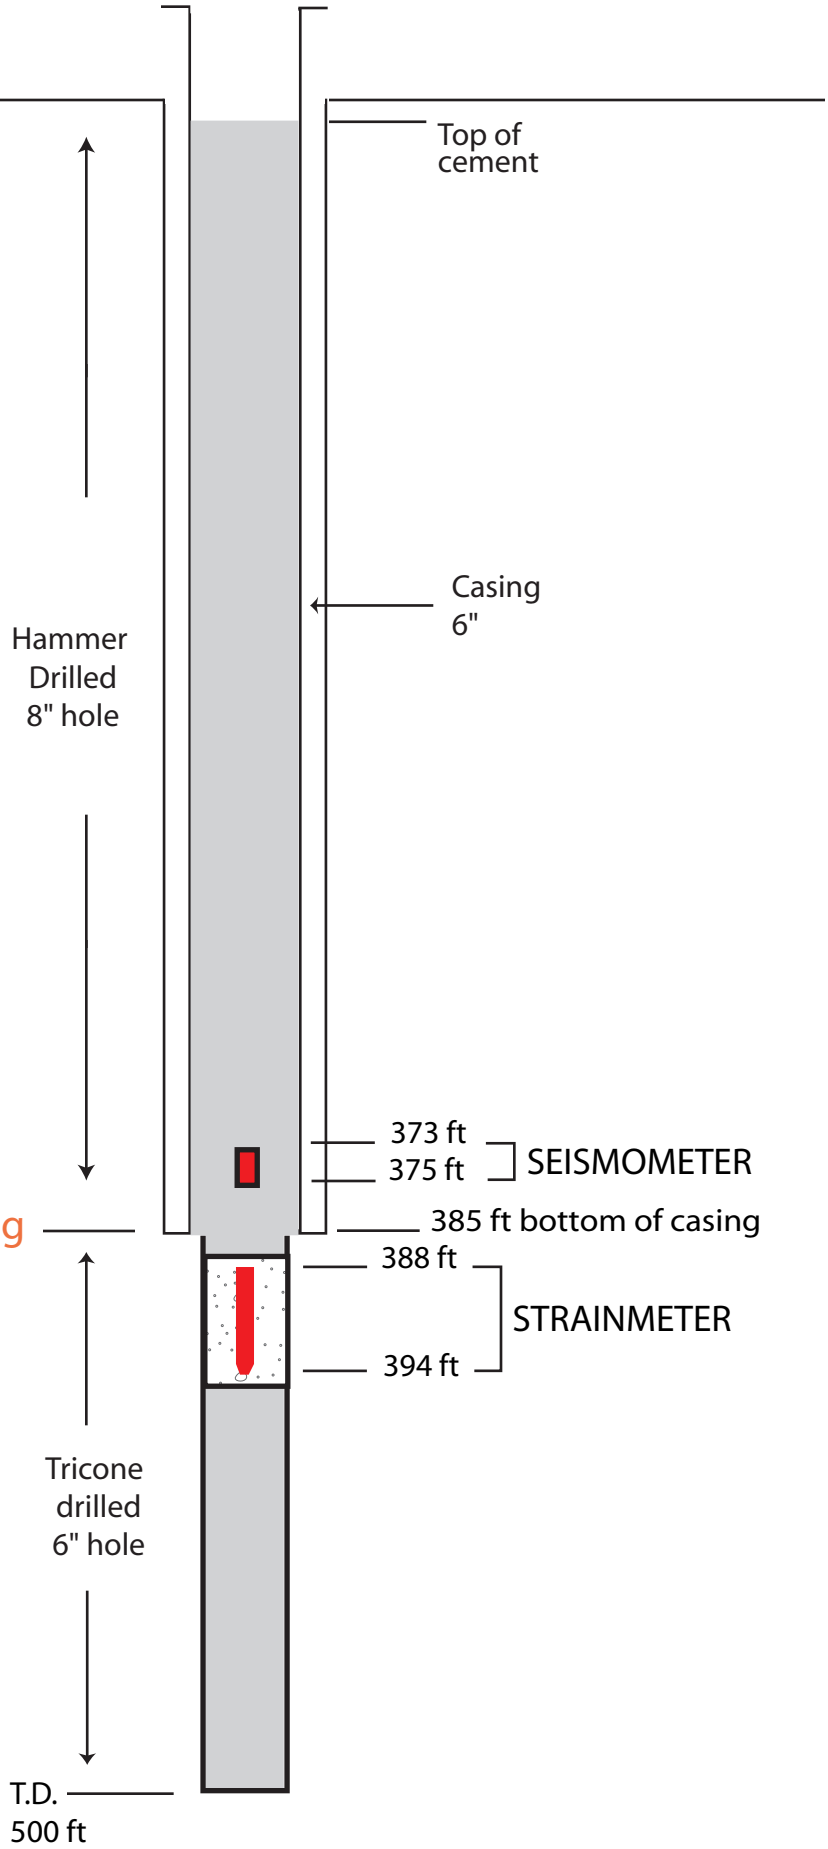

200 ft - water took on brown tint and penitration rate slowed, t=24.8 C

243 ft - rough drilling

269.5 ft ~100gpm

NOT TO SCALE

Cables not shown

all depths relative to top of casing

Last Updated 3 September 2008

397 ft - T = 46 C

412-413 ft - ashy

431 ft - fractures

434 ft - very rough drilling

435 ft - smoother dilling, 200 gpm

445 ft - more then 200gpm, T = 34.8 C

464 ft - rough drilling, T = 34.8 C

472 ft, 473-475 ft, 476 ft - rough drilling

495 ft - rough drilling, T = 34.5 C
